


1



Completed construction above the valve chamber.

2

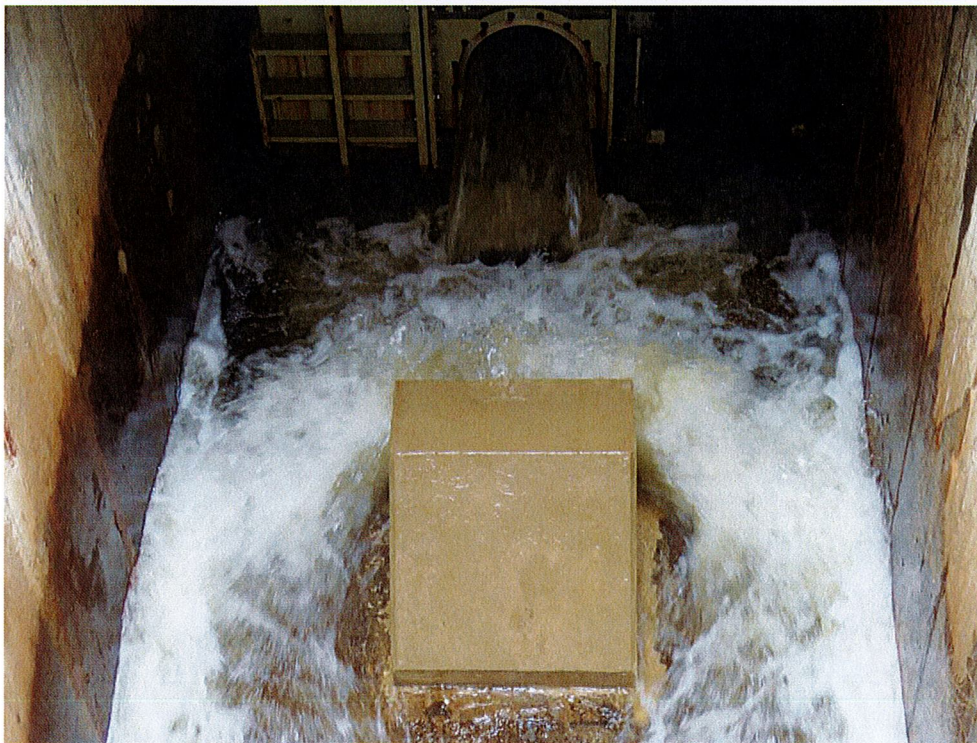

Completed valve chamber onstruction. Knife Gate valve in open position during construction pool head.



Wee Wah Lake & Pond No. 3  
Dam Rehabilitation Project  
Village of Tuxedo Park, New York



3



Auxiliary spillway structure showing completed capstone placement.

4



Auxiliary spillway granite veneer effacement of collar section of weir.






Completed Auxiliary Spillway capstone placement (grouting and anchoring not completed).

6



LLO knife gate valve correction of gate seating orientation.



Wee Wah Lake & Pond No. 3  
Dam Rehabilitation Project  
Village of Tuxedo Park, New York



7



Primary spillway forebay showing last segment of overpour construction.

8



Primary spillway forebay structure showing completed concrete construction.



CHA # 30855

Wee Wah Lake & Pond No. 3  
Dam Rehabilitation Project  
Village of Tuxedo Park, New York

June 29, 2018



9



Former LLO pipe (24" dia.) prior to backfilling with concrete.

10



Pond No. 3 completed LLO siphon system, old outlet abandonment and repointing.



**Wee Wah Lake & Pond No. 3  
Dam Rehabilitation Project  
Village of Tuxedo Park, New York**

CHA # 30855

June 29, 2018
